


# ArgoNeuT Status

Mitch Soderberg

6/24/2008

# Update

- Cryostat is sealed and being pumped down.
- Guard vacuums checked
- Inner cryostat pumped down to 0.3 Torr
- Need to pump outer vacuum to check.
- TPC Signal cables mounted on feedthrough.
- Some damage to cables during installation, due to sharp edges of shield pipe.
- Will assess during commissioning run, and potentially replace cables before move underground.

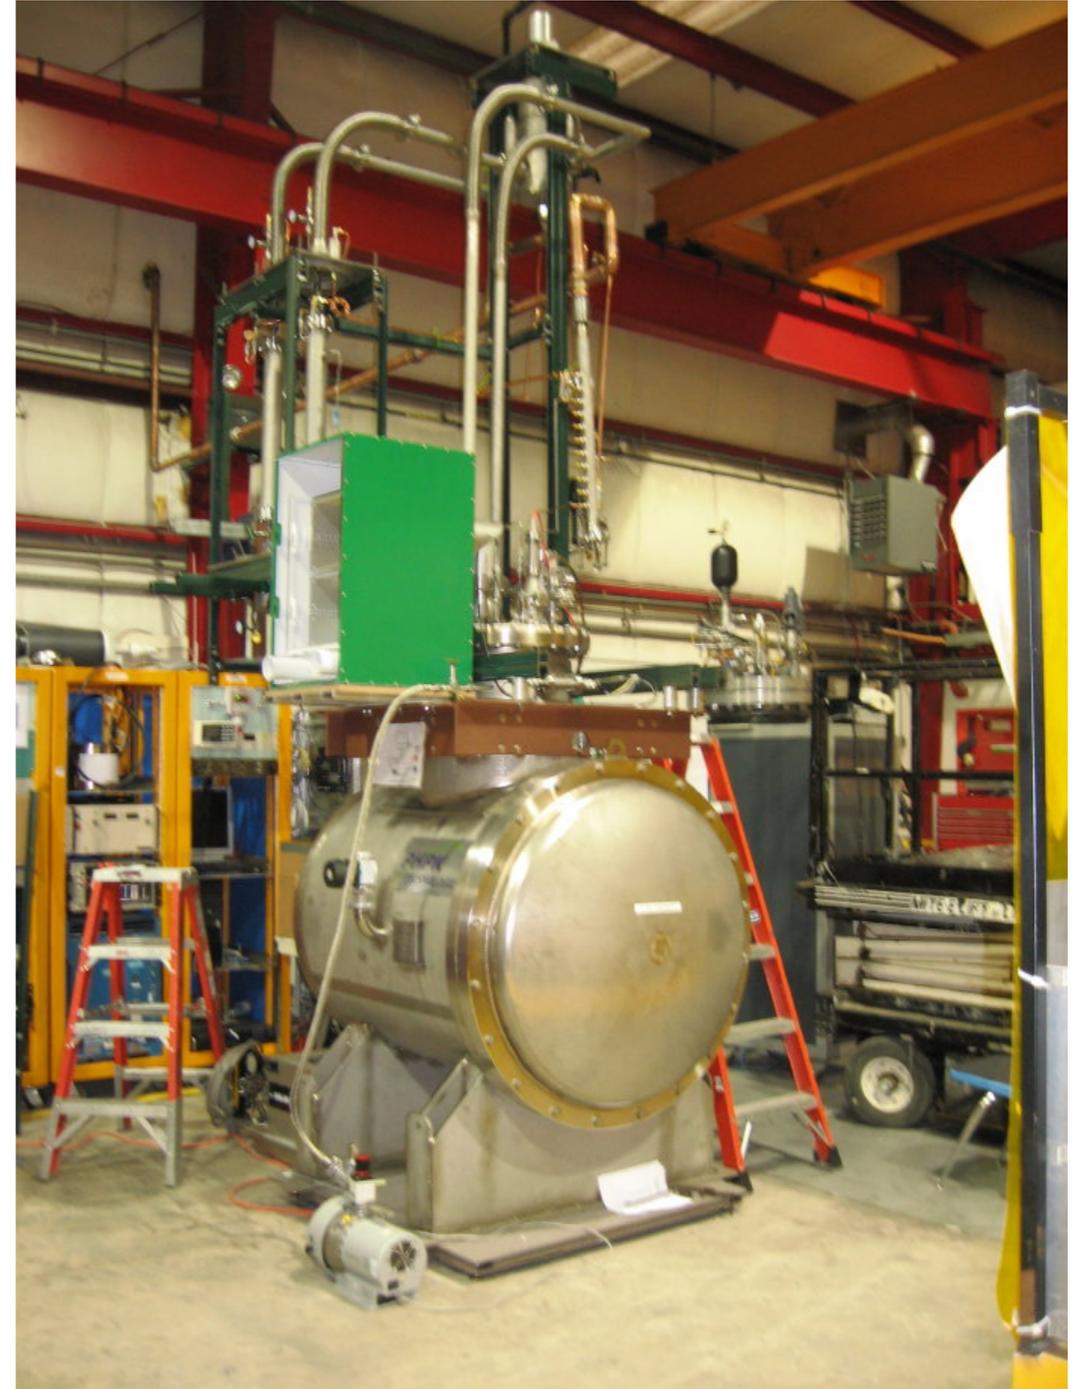

# To Do

- Hook up cryocooler to compressor / chilled-water (today / tomorrow).
- Insulate / regenerate filters (today / tomorrow).
- Install cable tray from electronics box over to rack (today).
- Install LAr fill line (today).
- Tidy up area before Thu.

## New items (work in progress):

- **E-LogBook:** <http://www-argoneut-crl.fnal.gov/argoneut/Index.jsp>
- **CVS:** <http://cdcv0.fnal.gov/cgi-bin/public-cvs/cvsweb-public.cgi/?cvsroot=t962cvs>
